

CITY OF STAMFORD

MAYOR
CAROLINE SIMMONS

DIRECTOR OF OPERATIONS
MATT QUINONES
Email: MQuinones@StamfordCT.gov




CITY ENGINEER
LOUIS CASOLO, JR., P.E.
Email: LCasolo@StamfordCT.gov

OFFICE OF OPERATIONS ENGINEERING BUREAU

INTEROFFICE MEMORANDUM

To: Matt Quinones
Director of Operations

From: Lou Casolo, P.E. 
City Engineer

Date: July 14, 2023

Subject: Demolition and Abatement of the Old Police Station – Bid No. S-6784
Change Order No. 2 – Additional ACM Disposal

DOES REQUIRE BOARD OF FINANCE APPROVAL

Please find attached two copies of change order number two (2). This change order in the amount of \$ 290,404.76 explained and documented, are field revision issues, which were unknown at the time of bidding and are considered unforeseen conditions. As this change order exceeds the original contract amount by more than 15% this does require the Board of Finance approval.

The source of funding for this change order is included in the project's appropriation and requires no additional funding.

Upon your approval, please submit this Change Order to the Mayor for her submission to the Board of Finance for their review and approval. Upon receiving the Board of Finance approval and Mayor's signature, please then return it to our Bureau for processing.

Should you have any questions, please feel free to contact me at 977-5796

cc: Domenic Tramontozzi P.E., Sr. Construction Manager

Reg. No. 203

TITLE: Additional ACM Disposal
PROJECT: Demolition of Old Police Station
805 Bedford Street

Bid S-6784

Date: 6/23/2023

TO: Stamford Wrecking Company
30 Nutmeg Drive
Trumbull, CT 06611

DESCRIPTION OF CHANGE:

COR 2 Additional cost for transportation and disposal of asbestos containing materials on the concrete foundation walls above what was included in the contract documents. Work was overseen and verified by both BL Companies (construction administrator) and Eagle Environmental (environmental monitoring consultant).

Increase \$ 290,404.76


These additional quantities were unknown at the time of bidding and are considered unforeseen conditions. There are sufficient funds available in the capital account to cover this additional cost. Board of Finance approval is required as the change order exceeds 15% of the contract value.


Net Increase \$ 290,404.76


The Original Contract Sum Was	\$	867,518.00
Net Change by Previously Authorized Requests and Changes		\$5,188.50
Contract Sum prior to this Change Order	\$	872,706.50
Contract Sum Will Be Increased		\$290,404.76
New Contract Sum Including This Change Order	\$	1,163,111.26
The Contract Time Will Be Changed		0 Days

Accepted:
Stamford Wrecking
By: 
Date: 7/3/2023

Sr. Construction Manager
By: 
Date: 7/7/23

City Engineer
By: 
Date: 7/14/23

Director of Operations
By: 
Date: 7-18-23

Mayor, City of Stamford
By: 
Date: 7/21/23

Stamford Wrecking Company

30 Nutmeg Drive
Trumbull, CT 06611
Ph : (203) 380-8300

Change Request

To: Stamford, City of
888 Washington Blvd, 7th Fl
Stamford, CT 06901

Number: 2
Date: 4/28/23
Job: SW-STAM-1360 Police Station Demo, Stamford
Phone: 60

Description: Addiitonal ACM Disposal

Source: Other # EMAIL

We are pleased to offer the following specifications and pricing to make the following changes:

This proposal provides the additional cost for transportation and disposal of asbestos contaminated building materials above what was included in the contract documents, and as agreed upon by the City of Stamford and Stamford Wrecking Company as per the e-mail that transmitted this Change Request. The additional tonnage was calculated based on the following:

Total waste shipped - 2,158.88 tons
Included in contract - (471 tons)
Additional waste - 1,687.88 tons

Load average calculation:
2,158.88 tons shipped / 63 total loads = 34.27 tons/load
471 / 34.27 = 14 loads (rounded up)
Total loads - 63
Loads in contract - (14)
Additional loads - 49

Work performed by subcontractors:

Description	Quantity	Unit	Unit Price	Price
Non-Friable ACM Disposal	1,687.88	Ton(s)	\$167.00	\$281,875.96
Fuel Surcharge	49.00	Load	\$300.00	\$14,700.00
Credit for Unsuitable Soil Disposal	-1.00	Lump Sum	\$20,000.00	\$-20,000.00
			Subtotal:	\$276,575.96
			Subtotal:	\$276,575.96
	OH&P	\$276,575.96	5.00%	\$13,828.80
			Total:	\$290,404.76

The schedule is not affected by this change.

If you have any questions, please contact me at 203-380-8300.

Submitted by: Terlizzi, Bryan
Stamford Wrecking Company

Approved by: _____
Date: _____

Tramontozzi, Domenick

From: Olesen, Clare <colesen@Blcompanies.com>
Sent: Tuesday, February 21, 2023 4:12 PM
To: Tramontozzi, Domenick; Jenney, John, CCCA
Cc: Casolo, Louis
Subject: RE: Police Demo - Change Request 02 - Additional ACM Disposal

It looks like Eagle confirmed that 63 loads of ACM left the site. I agree ~471 tons of ACM were included in the contract and based on Eagle's confirmation of ACM loads this change order looks valid with an additional 49 loads.

Clare

Clare Olesen
Senior Project Manager
BL Companies | *Employee owned. Client driven.*



355 Research Parkway, Meriden, CT 06450
Cell (860) 519-3323 (preferred)
tel: 203.630.1406 | direct: 203.608.2496
fax: 203.608-2615
www.blcompanies.com

From: Tramontozzi, Domenick <DTramontozzi@StamfordCT.gov>
Sent: Tuesday, February 21, 2023 3:42 PM
To: Jenney, John, CCCA <jjenney@Blcompanies.com>; Olesen, Clare <colesen@Blcompanies.com>
Cc: Casolo, Louis <LCasolo@StamfordCT.gov>
Subject: RE: Police Demo - Change Request 02 - Additional ACM Disposal

John / Clare –

Circling back on this. I got the below feedback from Eagle Environmental on the submitted change order.

I have gone through our field records and have documented sixty three (63) loads of ACM building debris generated from the building demolition activities that match up against the manifests submitted by Stamford Wrecking. The manifest numbers match up against our field logs with the exception of one manifest that I could not find in Stamford's submittal package – Manifest number B-61801 is documented as having been issued on 6-22-2022 (this manifest number is included in my calculation of the 63 loads). I did not see this manifest in the submittal. We documented 63 loads leaving the site and their Change Order references 63 however they are missing the above noted manifest unless I missed it the 268 page submittal..

Eagle did not write the bid specifications for the project was not involved in any of the upfront bidding activities, contractual negotiations or bid award so we are at a loss to comment on the pricing aspect of the change order. Eagle was contracted to provide asbestos abatement monitoring and oversight services only. Our role was to strictly document how many loads of ACM debris were hauled off site as directed by Jeff Pardo. Furthermore, I do believe the reference to the unsuitable fill is not for asbestos building debris but rather for fill contaminated by some other source but not having authored the bidding documents I am at a loss to confirm this to be the case. This would be a question for BL Companies.

Based upon our review the total number of loads being quoted is correct. Please let me know if you have any other questions.

I guess we need to review and interpret rates etc. with what is called for in the contracts well as any scope that may have been eliminated if any by this disposal.

Thanks,
Domenic

From: Jenney, John, CCCA <jjenney@blcompanies.com>
Sent: Tuesday, February 07, 2023 6:55 AM
To: Tramontozzi, Domenick <DTramontozzi@StamfordCT.gov>; 'jeberhard@eagleenviro.com' <jeberhard@eagleenviro.com>; 'gmishler@eagleenviro.com' <gmishler@eagleenviro.com>
Cc: Casolo, Louis <LCasolo@StamfordCT.gov>; Jenney, John, CCCA <jjenney@blcompanies.com>
Subject: RE: Police Demo - Change Request 02 - Additional ACM Disposal

Good morning Domenick. I can participate, but I'm not available on Thursday. I reached out to Clare Olesen from our Environmental Group to see if she's available. She had a more active role on the environmental/waste side of this project and was part of some of these waste disposal discussions with Jeff Pardo. I'll confirm her availability.

Regards,

John D. Jenney, CCCA
Principal
Senior Construction Manager
BL Companies | *Employee owned. Client driven.*



We're growing! *Build your career at BL.*

Learn about opportunities [here](#).

355 Research Parkway, Meriden, CT 06450
tel: 203.630.1406 | direct: 203.608.2508
mobile: 203-666-6599 | fax: 203.630.2615
www.blcompanies.com

From: Tramontozzi, Domenick <DTramontozzi@StamfordCT.gov>
Sent: Monday, February 6, 2023 12:44 PM
To: 'jeberhard@eagleenviro.com' <jeberhard@eagleenviro.com>; 'gmishler@eagleenviro.com'

<gmishler@eagleenviro.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>

Cc: Casolo, Louis <LCasolo@StamfordCT.gov>

Subject: FW: Police Demo - Change Request 02 - Additional ACM Disposal

Jason / Gerald –

The City of Stamford received the attached change order for additional ACM disposal costs from Stamford Wrecking Company. From some notes that Jeff Pardo left us I believe that Eagle Environmental was assisting in tracking this work. Can you take a look at this information and let us know your thoughts.

Jeff Pardo did also state that the contract included an allowance for the removal and disposal of 10 truckloads of non-hazardous unsuitable material. Per Stamford Wrecking Company pay app this is valued at \$ 20,000.00. I have also included the Stamford Wrecking Company contract which does have unit pricing that may help in the evaluation.

We can schedule a zoom meeting maybe on Thursday 2/9 to discuss please let me know your availability.

John (BL) I know Julie has left BL can you let me know if you are the right person to be part of this meeting or should someone else at BL take part?

Thanks,
Domenic

From: Bryan Terlizzi <BTerlizzi@DemolitionServices.com>

Sent: Monday, February 06, 2023 11:12 AM

To: Tramontozzi, Domenick <DTramontozzi@StamfordCT.gov>

Subject: FW: Police Demo - Change Request 02 - Additional ACM Disposal

Good morning Domenick,

I finally received all the disposal manifests from Stamford PD allowing me to finalize the additional ACM disposal Change Request. Please review the attached. You can access the shipping records through the Dropbox link below.

<https://www.dropbox.com/sh/jq2o8tbdnzvcfjd/AAAADqwEARVhoz4o9F3Q8bfBa?dl=0>

Please issue a change order at your earliest convenience. If possible, I would like to get the final invoice, inclusive of the change order, submitted this month for processing.

Any questions, please call.

Bryan Terlizzi
Senior Project Manager



Stamford Wrecking Company

30 Nutmeg Drive, Trumbull, CT 06611

Office: 203-380-8300

Cell: 203-219-8042

BTerlizzi@demolitionservices.com

www.stamfordwrecking.com

From: Pardo, Jeff <JPardo@StamfordCT.gov>
Sent: Thursday, June 23, 2022 10:52 AM
To: Bryan Terlizzi <BTerlizzi@DemolitionServices.com>; Stephen Goldblum <SGoldblum@DemolitionServices.com>
Cc: Minkunas, Julie, RA <jminkunas@Blcompanies.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>; 'Jason Eberhard' <jeberhard@eagleenviro.com>; Gerald Mishler <gmishler@eagleenviro.com>; Byxbee, Kenneth <KByxbee@StamfordCT.gov>
Subject: RE: Police Demo

Yes, that is reasonable. Jerry will still keep track of where ACM is discovered and not shown on the contract documents. Additionally, it is the City's expectation that clean concrete will be removed from the foundation walls so only the areas with ACM are included in the asbestos waste disposal. See example photo attached.

From: Bryan Terlizzi <BTerlizzi@DemolitionServices.com>
Sent: Thursday, June 23, 2022 9:40 AM
To: Pardo, Jeff <JPardo@StamfordCT.gov>; Stephen Goldblum <SGoldblum@DemolitionServices.com>
Cc: Minkunas, Julie, RA <jminkunas@Blcompanies.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>; 'Jason Eberhard' <jeberhard@eagleenviro.com>; Gerald Mishler <gmishler@eagleenviro.com>; Byxbee, Kenneth <KByxbee@StamfordCT.gov>
Subject: RE: Police Demo

Good morning Jeff,

Thanks for meeting at the site yesterday afternoon.

The following is a recap of our discussion and what we agreed upon regarding additional ACM.

We agreed that additional asbestos would be calculated by subtracting the quantity of asbestos included in the specifications from the actual quantity of asbestos as verified by certified weight tickets.

The baseline quantity conversion is as follows:

Concrete Foundation Walls

Specified quantity – 2,650 SF x 1' Thick = 2,650 CF x 150 [lbs.CF](#) = 397,500 lbs / 2,000 lbs/ton = 199 tons

Dampproofing Behind Brick Walls

Specified quantity – 6,760 SF x 10" Thick = 5,633 CF / 27 = 209 CY x 1.3 Conversion = 272 tons

SWC is responsible for 471 tons of asbestos waste disposal. The City is responsible for the verified tonnage over 471 tons which will be applied to the disposal unit price approved by the City.

Please review and reply confirming our agreement.

Thanks,
Bryan

From: Bryan Terlizzi
Sent: Wednesday, June 22, 2022 11:12 AM
To: 'Pardo, Jeff' <JPardo@StamfordCT.gov>; Stephen Goldblum <SGoldblum@DemolitionServices.com>
Cc: Minkunas, Julie, RA <jminkunas@Blcompanies.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>; 'Jason

Eberhard' <jeberhard@eagleenviro.com>; Gerald Mishler <gmishler@eagleenviro.com>; Byxbee, Kenneth <KByxbee@StamfordCT.gov>

Subject: RE: Police Demo

I think it would be good to meet at the site to streamline the rest of the review process. Are you available at 1 pm?

From: Pardo, Jeff <JPardo@StamfordCT.gov>

Sent: Wednesday, June 22, 2022 11:03 AM

To: Bryan Terlizzi <BTerlizzi@DemolitionServices.com>; Stephen Goldblum <SGoldblum@DemolitionServices.com>

Cc: Minkunas, Julie, RA <jminkunas@Blcompanies.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>; 'Jason Eberhard' <jeberhard@eagleenviro.com>; Gerald Mishler <gmishler@eagleenviro.com>; Byxbee, Kenneth <KByxbee@StamfordCT.gov>

Subject: RE: Police Demo

OK, look forward to it. If you would like me to be on site when are there, let me know.

From: Bryan Terlizzi <BTerlizzi@DemolitionServices.com>

Sent: Wednesday, June 22, 2022 10:23 AM

To: Pardo, Jeff <JPardo@StamfordCT.gov>; Stephen Goldblum <SGoldblum@DemolitionServices.com>

Cc: Minkunas, Julie, RA <jminkunas@Blcompanies.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>; 'Jason Eberhard' <jeberhard@eagleenviro.com>; Gerald Mishler <gmishler@eagleenviro.com>; Byxbee, Kenneth <KByxbee@StamfordCT.gov>

Subject: RE: Police Demo

Jeff,

I was out of the office the last two days. I am in the process of reviewing the information you presented. I am visiting the site this afternoon to gather more information needed to complete my review. I will provide a formal response before the end of the week. I will ensure that questionable items will not impede progress.

Thanks,
Bryan

From: Pardo, Jeff <JPardo@StamfordCT.gov>

Sent: Tuesday, June 21, 2022 11:42 AM

To: Bryan Terlizzi <BTerlizzi@DemolitionServices.com>; Stephen Goldblum <SGoldblum@DemolitionServices.com>

Cc: Minkunas, Julie, RA <jminkunas@Blcompanies.com>; Jenney, John, CCCA <jjenney@Blcompanies.com>; 'Jason Eberhard' <jeberhard@eagleenviro.com>; Gerald Mishler <gmishler@eagleenviro.com>; Byxbee, Kenneth <KByxbee@StamfordCT.gov>

Subject: Police Demo

Bryan

On 6/15/22 I sent you an email with my calculations regarding extras and deducts of non-friable ACM based on field conditions. Two of the foundations that were removed that do have ACM are not being removed. Eagle needs to know how those foundations are being considered. They are hampering your excavator's ability to continue working effectively. If you want to keep track of the foundations that will be additional to the contract and those that will be a deduct, we can do that easy enough.

Just so you know, your original schedule for Mass Demo (Uncontaminated Building Material), Mass Demolition (AWP Asbestos Waterproofing) and Mass Demolition Slab & Foundation (Uncontaminated Building Materials) had a duration

of 25 working days. Currently, building demolition began April 11th, including today, Stamford Wrecking is at 50 working days and the work may require an additional two weeks to complete, perhaps more. Any perceived delay Stamford Wrecking believes they encountered has nothing to do with these additional 25 days and counting for the mass demolition.

I need to get this project finished. I'm paying Eagle by the day and many of the days there is very little activity.

Photo 4-22-22 2 was the first time I thought of taking a photo from on top of the courthouse garage, this is 10 days into the Mass Demolition activity. Photo 5-13-22 1 is 25 days into the Mass Demolition activity. Photo 6-21-22 1 is this morning, 50 days into the Mass Demolition activity.

Jeffrey Pardo
Construction Manager
City of Stamford
888 Washington Boulevard
Stamford, CT 06905
203-977-5227
jpardo@stamfordct.gov

Stamford Wrecking Company

30 Nutmeg Drive
 Trumbull, CT 06611
 Ph : (203) 380-8300

Change Request

To: Stamford, City of
 888 Washington Blvd, 7th Fl
 Stamford, CT 06901

Number: 2
Date: 2/6/23
Job: SW-STAM-1360 Police Station Demo, Stamford
Phone: 60

Description: Additonal ACM Disposal


Source: Other # EMAIL

We are pleased to offer the following specifications and pricing to make the following changes:

This proposal provides the additional cost for transportation and disposal of asbestos contaminated building materials above what was included in the contract documents, and as agreed upon by the City of Stamford and Stamford Wrecking Company as per the e-mail that transmitted this Change Request. The additional tonnage was calculated based on the following:

Total waste shipped - 2,158.88 tons
 Included in contract - (471 tons)
 Additional waste - 1,687.88 tons

Load average calculation:
 2,158.88 tons shipped / 63 total loads = 34.27 tons/load
 471 / 34.27 = 14 loads (rounded up)
 Total loads - 63
 Loads in contract - (14)
 Additional loads - 49

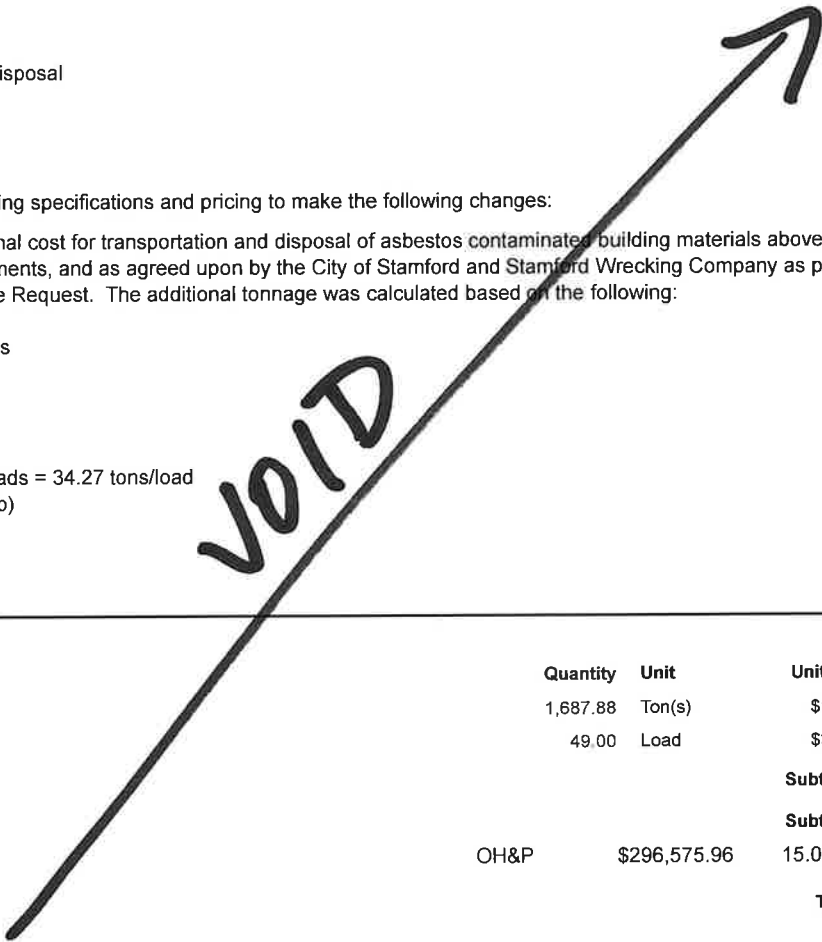

Work performed by subcontractors:

Description	Quantity	Unit	Unit Price	Price
Non-Friable ACM Disposal	1,687.88	Ton(s)	\$167.00	\$281,875.96
Fuel Surcharge	49.00	Load	\$300.00	\$14,700.00
			Subtotal:	\$296,575.96
			Subtotal:	\$296,575.96
	OH&P	\$296,575.96	15.00%	\$44,486.39
			Total:	\$341,062.35

The schedule is not affected by this change.

If you have any questions, please contact me at 203-380-8300.

Submitted by: Terlizzi, Bryan
 Stamford Wrecking Company

Approved by: _____
 Date: _____

Date	Ticket #	truck_lic	Container	Generator	Location	Gross Weight	Tare Weight	Weight
08/04/2022	420526	41	Trailer dump	805 Bedford St	CT, Stamford	105820	33440	36.19
08/04/2022	420546	95	Trailer dump	805 Bedford St	CT, Stamford	83440	35800	23.82
						Total		60.01
08/05/2022	420579	110	Trailer dump	805 Bedford St	CT, Stamford	111960	32500	39.73
08/05/2022	420589	145/114	Trailer dump	805 Bedford St	CT, Stamford	116160	33460	41.35
08/05/2022	420591	115	Trailer dump	805 Bedford St	CT, Stamford	116800	33340	41.73
08/05/2022	420596	403	Trailer dump	805 Bedford St	CT, Stamford	114480	32080	41.20
08/05/2022	420607	113	Trailer dump	805 Bedford St	CT, Stamford	128540	33100	47.72
						Total		211.73

Date	Ticket #	Transporter	truck_lic	Container	Generator	Location	Gross Weig	Tare Weig	Weight
07/05/2022	419043	LG/Shaw	14	Trailer dump	805 Bedford St	CT, Stamford	95200	33240	30.98
07/05/2022	419011	Sterling	153/103	Trailer dump	805 Bedford St	CT, Stamford	83820	30960	26.43
						Total			57.41
07/07/2022	419126	Alterio/The Boss	012	Trailer dump	805 Bedford St	CT, Stamford	102520	31940	35.29
07/07/2022	419117	Alterio/Steam Valley	414	Trailer dump	805 Bedford St	CT, Stamford	84320	33620	25.35
						Total			60.64
07/11/2022	419281	Arsenberger Trucking	95	Trailer dump	805 Bedford St	CT, Stamford	80420	35800	22.31
						Total			22.31
07/26/2022	420012	Arsenberger Trucking	96	Trailer dump	805 Bedford St	CT, Stamford	83120	33360	24.88
07/26/2022	420010	Arsenberger Trucking	101	Trailer dump	805 Bedford St	CT, Stamford	84820	35600	24.61
						Total			49.49
07/27/2022	420088	Brown/Weisel	403	Trailer dump	805 Bedford St	CT, Stamford	107000	32080	37.46
07/27/2022	420072	Arsenberger Trucking	99	Trailer dump	805 Bedford St	CT, Stamford	83320	35340	23.99
						Total			61.45

Date	Ticket #	Transporter	truck_lic	Container	Generator	Location	Gross Weight	Tare Weight	Weight
06/08/2022	417949	Alterio Trucking	115	Trailer dump	805 Bedford St	CT, Stamford	100000	33340	33.33
06/08/2022	417950	Alterio Trucking	104	Trailer dump	805 Bedford St	CT, Stamford	95120	33640	30.74
06/08/2022	417957	ICC Trucking	43	Trailer dump	805 Bedford St	CT, Stamford	113240	36840	38.20
							Total		102.27
06/09/2022	418004	Brown/Miller	8656	Trailer dump	805 Bedford St	CT Stamford	121780	31900	44.94
06/09/2022	418017	Brent Brown Trucking	624	Trailer dump	805 Bedford St	CT, Stamford	116420	33960	41.23
06/09/2022	418023	Kevin Bean	314	Trailer dump	805 Bedford St	CT, Stamford	110860	37040	36.91
							Total		123.08
06/10/2022	418057	Brown Transport	145	Trailer dump	805 Bedford St	CT, Stamford	106660	33460	36.60
06/10/2022	418074	Alterio Trucking	114	Trailer dump	805 Bedford St	CT, Stamford	116060	33120	41.47
							Total		78.07
06/13/2022	418134	Alterio/Steam Valley	414	Trailer dump	805 Bedford St	CT, Stamford	81620	33620	24.00
							Total		24.00
06/23/2022	418581	Alterio Trucking	105/T18	Trailer dump	805 Bedford St	CT, Stamford	118120	31960	43.08
							Total		43.08
06/24/2022	418648	Arsenberger Trucking	97	Trailer dump	805 Bedford St	CT, Stamford	79020	35620	21.70
06/24/2022	418657	Alterio Trucking	104	Trailer dump	805 Bedford St	CT, Stamford	100780	33640	33.57
06/24/2022	418660	Brown/Weisel	403	Trailer dump	805 Bedford St	CT, Stamford	102520	32080	35.22
							Total		90.49
06/27/2022	418743	Alterio/Weaver	132	Trailer dump	805 Bedford St	CT, Stamford	103480	33080	35.20
							Total		35.20
06/28/2022	418817	Brown/Weisel	403/403A	Trailer dump	805 Bedford St	CT, Stamford	95480	32080	31.70
							Total		31.70
06/29/2022	418840	Weigle Trucking	105	Trailer dump	805 Bedford St	CT, Stamford	104800	31960	36.42
06/29/2022	418843	Weigle Trucking	104	Trailer dump	805 Bedford St	CT, Stamford	111540	31440	40.05
							Total		76.47
06/30/2022	418921	Brown/Weisel	403	dump	805 Bedford St	CT, Stamford	104900	32080	36.41
							Total		36.41

Date	Ticket #	Transporter	truck_lic	Container	Generator	Location	Gross Weight	Tare Weight	Weight
06/01/2022	417665	Alterio Trucking	105	Trailer dump	805 Bedford St	CT, Stratford	95040	31960	31.54
06/01/2022	417687	Alterio Trucking	116	Trailer dump	805 Bedford St	CT, Stamford	80700	33620	23.54
06/01/2022	417688	Alterio/The Boss	012	Trailer dump	805 Bedford St	CT, Stamford	84560	31940	26.31
							Total		81.39
06/02/2022	417714	Alterio/Steam Valley	414	Trailer dump	805 Bedford St	CT, Stamford	83720	33620	25.05
06/02/2022	417717	Alterio Trucking	104	Trailer dump	805 Bedford St	CT, Stamford	100740	33640	33.55
06/02/2022	417724	Alterio Trucking	113	Trailer dump	805 Bedford St	CT, Stamford	126700	33100	46.80
06/02/2022	417746	Alterio Trucking	115	Trailer dump	805 Bedford St	CT, Stamford	116320	33340	41.49
							Total		146.89
06/03/2022	417770	Alterio Trucking	105	Trailer dump	805 Bedford St	CT, Stamford	107420	31960	37.73
06/03/2022	417785	Alterio Trucking	116	Trailer dump	805 Bedford St	CT Stamford	80980	33620	23.68
							Total		61.41
06/06/2022	417846	Alterio Trucking	115	Trailer dump	805 Bedford St	CT, Stamford	101000	33340	33.83
06/06/2022	417847	Alterio Trucking	114	Trailer dump	805 Bedford St	CT, Stamford	125860	33120	46.37
06/06/2022	417848	Alterio Trucking	113	Trailer dump	805 Bedford St	CT, Stamford	126700	33100	46.80
							Total		127.00
06/07/2022	417892	Alterio Trucking	105/T18	Trailer dump	805 Bedford St	CT, Stamford	113520	31960	40.78
06/07/2022	417910	ICC Trucking	34	Trailer dump	805 Bedford St	CT, Stamford	76680	36180	20.25
							Total		61.03

Date	Ticket #	Transporter	truck_lic	Container	Generator	Location	Gross Weight	Tare Weight	Weight
05/24/2022	417451	LG/JR	13	Trailer dump	805 Bedford St	CT, Stamford	118440	34660	41.89
05/24/2022	417440	LG Trucking	2803/T2803	Trailer dump	805 Bedford St	CT, Stamford	129740	36200	46.77
05/24/2022	417435	Weigle Trucking	104/104A	Trailer dump	805 Bedford St	CT, Stamford	100980	31440	34.77
							Total		123.43
05/25/2022	417496	ICC Trucking	42	Trailer dump	805 Bedford St	CT, Stamford	91460	33720	28.87
05/25/2022	417495	ICC Trucking	41	Trailer dump	805 Bedford St	CT, Stamford	93420	33740	29.84
05/25/2022	417494	ICC Trucking	2	Trailer dump	805 Bedford St	CT, Stamford	92420	34740	28.84
05/25/2022	417489	Alterio/The Boss	012	Trailer dump	805 Bedford St	CT, Stamford	91440	31940	29.75
05/25/2022	417472	Alterio Trucking	115	Trailer dump	805 Bedford St	CT, Stamford	115540	33340	41.10
05/25/2022	417466	Alterio/Steam Valley	414	Trailer dump	805 Bedford St	CT, Stamford	87620	33620	27.00
							Total		185.40
05/26/2022	417545	LG Trucking	2801/T2801	Trailer dump	805 Bedford St	CT, Stamford	129420	34580	47.42
05/26/2022	417528	Alterio Trucking	113/T23	Trailer dump	805 Bedford St	CT, Stamford	114960	32900	41.03
05/26/2022	417523	Alterio Trucking	104/T16	Trailer dump	805 Bedford St	CT, Stamford	102500	33640	34.43
05/26/2022	417521	Alterio Trucking	132/14	Trailer dump	805 Bedford St	CT, Stamford	100540	33080	33.73
							Total		156.61
05/27/2022	417583	Alterio/The Boss	012	Trailer dump	805 Bedford St	CT, Stamford	87940	31940	28.00
							Total		28.00
05/31/2022	417610	Steam Valley	414/10A	Trailer dump	805 Bedford St	CT, Stamford	81440	33620	23.91
							Total		23.91



Stamford Wrecking Company
Attn: Mr. Bryan Terlizzi
30 Nutmeg Drive
Trumbull, CT 06611

May 26, 2022

PROJECT: Stamford, CT

Dear Mr. Terlizzi:

Scope of Work:

PRO-TECK, LLC is pleased to submit the following proposal to provide the transportation and disposal of non friable asbestos debris from the above mentioned project location. Transport all waste to a fully permitted asbestos landfill.

Cost:

Item/Description	Unit	Unit Price
Transportation and Disposal	Ton	\$167.00
Fuel Surcharge	Load	\$300.00

Pricing excludes any applicable state sales tax

A 23 ton minimum charge will apply to all loads

Benefits:

- Fully Insured.
- All paperwork in accordance with Federal & State guidelines to be prepared and distributed by Pro-Teck, LLC.

General Conditions:

- Loading is the responsibility of the Site Contractor.
- Purchase and lining of the trailers is the responsibility of the Site Contractor.
- A signed generator waste profile will be required for each waste stream before project commencement.
- Manifests/Shipping documents to be provided by Pro-Teck, LLC.
- Pro-Teck, LLC must have free and easy site access.
- Loading/Unloading demurrage or on-site delay time in excess of 1 hour after scheduled load time will be charged at \$125.00 per hour/per truck.
- Safety and tailgate meetings are billable from minute one.
- Gross weight not to exceed DOT limits.
- No free liquids.
- Pricing is subject to off spec charges should waste not meet acceptance criteria or information provided on waste profile.
- Truck called for "not used" will be invoiced accordingly.
- All cancellations require a 24-hour notice prior to the scheduled project date. A cancellation fee will apply if cancellations are not made prior to the 24-hour period.
- Pricing and scheduling based on availability at all facilities.
- Pricing based on work performed during normal business hours.
- Prevailing wage rates and certified payrolls do not apply.

Limited Liability Company

An equal opportunity employer



- Any change order conditions due to project overruns must be brought to the attention of Pro-Teck, LLC immediately and will be priced accordingly.
- Retainage will not be held on any payments made to Pro-Teck, LLC.
- Pricing is valid through May 31, 2022.
- Terms are Net 30 from date of invoice issued by Pro-Teck, LLC. We accept MasterCard, Discover, American Express and Visa as payment options. A finance surcharge will apply to all credit card payments.

Authorization to Proceed:

- Before Pro-Teck, LLC can begin work on this project, we require that you return a signed copy of the proposal authorizing us to proceed with the work described above. Please retain a copy of the original proposal for your records.
- Your authorization to proceed also acknowledges payment terms of **Net 30** from date of invoice issued by Pro-Teck, LLC. We accept MasterCard, Discover, American Express and Visa as payment options. A finance surcharge will apply to all credit card payments.

I hope this information is complete and helpful, and as always, thank you for considering Pro-Teck, LLC as your full service transportation and disposal company.

Sincerely,



Billy Torello
Principal Member

Signature _____

Title & Date _____
Your signature above will approve all pricing as well as general conditions herein.

Limited Liability Company



An equal opportunity employer
